

Hallsville Quarter Phase 3

Issue 07 – December 2020



A development by

linkcity

Dear Neighbours,

Welcome to the December 2020 issue of the Hallsville Quarter Phase 3 development newsletter, looking at the latest progress achieved and upcoming milestones.

Works progress

We shall be installing additional tower cranes over two weekends in December, from 08:00am to 18:00pm, minimising health and safety risks and impact on highways traffic around the site. There will be large delivery trucks and mobile cranes travelling to/from the site during the installation.


The noise level should remain very low and we will minimize activities during the early morning.

- ⇒ TC1 (block E) erection on 5th & 6th December 2020
- ⇒ TC2 (block E&D1) erection on 12th & 13th December 2020
- ⇒ In the event of adverse weather conditions, we might need to postpone one of the installations until the weekend of the 19th & 20th December 2020.

The main construction works has progressed as follows:

-) Foundations in blocks E and F: (piles caps and ground beams) are progressing well
-) Block F: Structural slab and walls at basement level have started
-) Block D2: first-floor slab & walls are progressing well
-) Below ground services have started
-) The hoarding branding was installed and includes photographs and artwork designed and photographed by the local community in collaboration with Newham Council

The site installation drawing above right shows the location of each of the blocks mentioned.

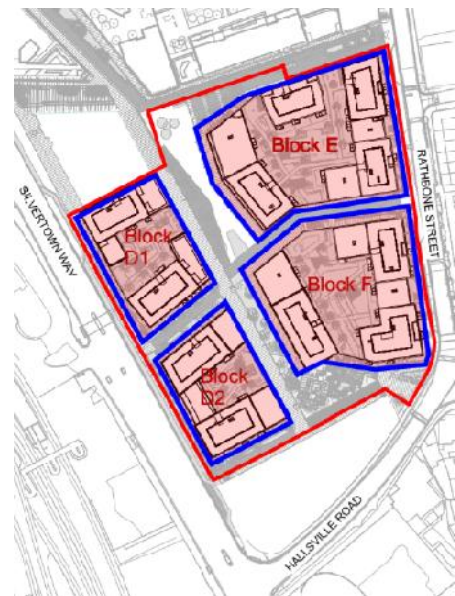

Events

We have partnered up with Solutions for the Planet and will be participating in a STEM challenge with one of the local schools (Stratford Academy). This will be launched in December and runs until April 2021. We will share more details with you after the launch. We are also working with the local DWP providing some workshops and in 2021 hosting some work experience opportunities.



Shared innovation

www.bouygues-uk.com

Your safety is our concern

Bouygues UK takes every precaution to keep you safe throughout the construction process.

At all times, our site will be secure and surrounded by fencing but building sites can be hazardous places:

- We dig deep holes
- We erect scaffolding
- We use large, noisy machinery

Please do not enter the construction site, unless it is part of a pre-arranged visit by our project team.

- Our operatives and staff are trained to work safely

Please help us to keep you and children safe, and take extra care during the school holidays.

Considerate Constructors Scheme

Bouygues UK firmly supports the aims of the Considerate Constructors Scheme. All of our sites are registered with the Scheme, and regular visits from the Considerate Constructors monitor will help us to ensure that we continue to improve our performance in showing full respect for:

-) Appearance
-) Community
-) Environment
-) Safety
-) Workforce

Please let us know if you have any concerns.

Our contact details are on the newsletter that you should regularly receive or on the site hoardings.

If you would like further information regarding the Scheme you can visit their website at www.ccscheme.org.uk

Standard site working hours are:

Monday to Friday:
7:30am-7pm

Saturday):
8am-1pm

Want to speak to us?

For more information about the development, please go to <https://hallsvillequarter.co.uk/whats-happening/>. In the next few months, we will update the website with the latest news.

Communication and Community Liaison

We are committed to working with the local community and keeping clear and open lines of communication throughout the construction phase. We have appointed Myra Carino as our Resident Liaison Officer. Please write to us should you have any questions or

Your contacts



Left: Myra Carino
Senior Project Assistant & Resident Liaison Officer
Tel No: 0800 083 7286
Email: myra.carino@bouygues-uk.com

Right: Lisa Ashworth
Social Value Advisor
Email: lisa.ashworth@bouygues-uk.com



Shared innovation

www.bouygues-uk.com
